

# NR2DT-09: Step 9 — Cutover, Rollback & Decommission

**Series:** NR2DT — New Relic to Dynatrace Migration Steps | **Notebook:** 9 of 10 |  
**Created:** April 2026 | **Last Updated:** 08/27/2026

## Overview

**Goal of this step:** complete the cutover from NR to DT. Halt NR ingest, archive NR artifacts, and confirm DT is the sole source of truth. Rollback plan stays valid for 30+ days.

Procedural — see **NRLC-08** (rollback manifest mechanics) and **NRLC-09** (toolchain reference) for depth.

## Table of Contents

- 1. [Cutover Sequence](#)
- 2. [Rollback Plan](#)
- 3. [Decommission NR](#)
- 4. [Step Exit Criteria](#)

## Prerequisites

| Requirement | Details                                          |
|-------------|--------------------------------------------------|
| Audience    | Migration lead + assigned engineer for this step |
| Completed   | NR2DT-08 — Validate                              |


| Requirement     | Details                                                     |
|-----------------|-------------------------------------------------------------|
| Format          | Procedural step — use as a runbook; defer to NRLC for depth |
| NRLC deep dives | NRLC-08 (rollback), NRLC-09 (toolchain)                     |

# 1. Cutover Sequence

Cutover is per-component, sequenced.

| Order | Component  | Cutover Action                                                                  |
|-------|------------|---------------------------------------------------------------------------------|
| 1     | Dashboards | Disable NR dashboard sharing; communicate DT URLs to consumers                  |
| 2     | Synthetics | Disable NR synthetic monitors (one type at a time)                              |
| 3     | Alerts     | Silence remaining NR alert policies (last to silence: critical incident routes) |
| 4     | SLOs       | Disable NR SLO reports; switch SLA dashboard data source to DT                  |
| 5     | Logs       | Stop dual-shipping; NR log ingest disabled per source                           |

**Halt criteria:** if any cutover step surfaces a regression, **stop and roll back that component**. Don't proceed to the next.

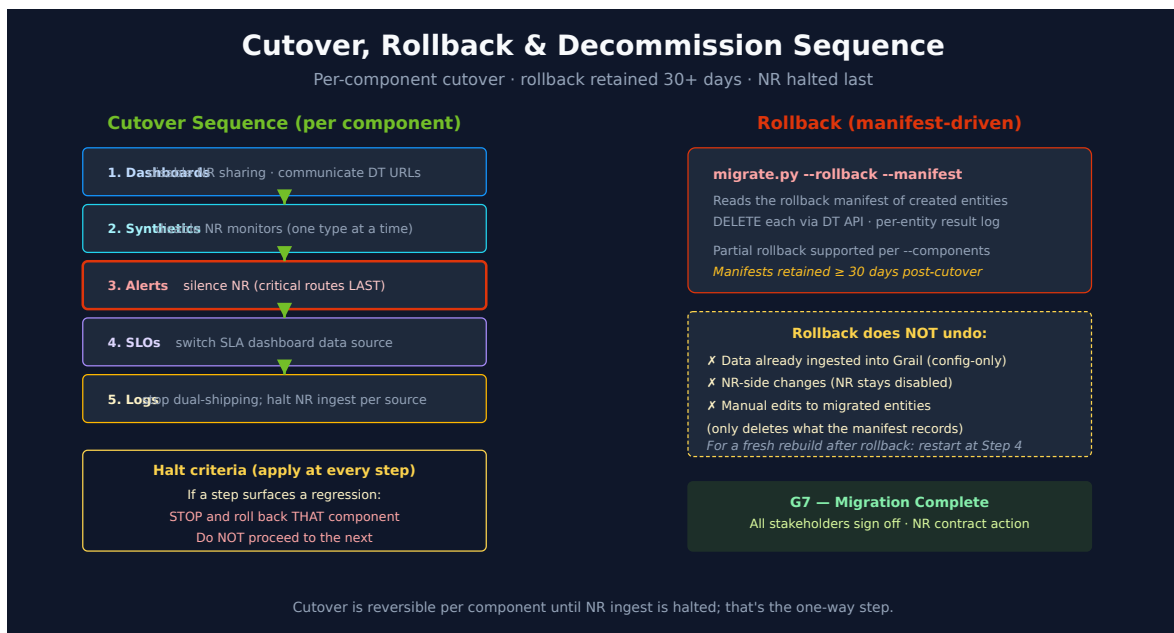

## 2. Rollback Plan

---

Every migration run produced a rollback manifest. Retain for **at least 30 days** post-cutover.

### Rollback command

```
python3 migrate.py migrate --rollback run-2026-04-14.json
```

The rollback:

1. Reads the manifest of created entities
2. Calls DELETE on each via DT API
3. Logs each deletion (succeeded / failed / skipped)
4. Produces a rollback report

**Partial rollback:** roll back one component only by filtering the manifest:

```
python3 migrate.py migrate --rollback run-2026-04-14.json --components  
dashboards
```

### What rollback DOES NOT undo:

- Data already ingested into Grail (configuration-only rollback)
- NR-side changes (NR dashboards stay disabled even after rollback)
- Manual edits to migrated entities (only deletes what the manifest records)

If you need a full rebuild after rollback, treat it as a fresh migration starting from Step 4 (translation is still valid).

## 3. Decommission NR

---

Final-stage cleanup. Sequenced for safety.

| Order | Action                                          | Reversible?              |
|-------|-------------------------------------------------|--------------------------|
| 1     | Disable NR alert routing (Workflows / channels) | Yes — re-enable in NR UI |

| Order | Action                                                     | Reversible?        |
|-------|------------------------------------------------------------|--------------------|
| 2     | Set NR dashboards to private / read-only                   | Yes                |
| 3     | Halt NR ingest per source (uninstall / reconfigure agents) | Yes (reinstall)    |
| 4     | Export NR account snapshot for archive                     | One-way            |
| 5     | Cancel NR contract / reduce seat count                     | Per contract terms |

**Decommission gate G9:** all stakeholders sign off that DT is operational and NR is no longer needed.

## 4. Step Exit Criteria

---

### G9 — Migration Complete

- ☐ All components cut over to DT
- ☐ Rollback manifests retained per retention policy ( $\geq 30$  days)
- ☐ NR alert routing disabled
- ☐ NR dashboards archived / set to read-only
- ☐ NR ingest halted at all sources
- ☐ NR account snapshot exported and stored
- ☐ All stakeholders signed off on completion

**Next step: NR2DT-99 — Best Practice Summary** (post-mortem and ongoing best practices).

---

*This notebook was AI-generated from community-submitted and publicly available sources, including the open-source [NewRelic-to-Dynatrace-Migration-Utilities](#), [nrql-engine](#), and [nrql-translator](#) projects. This notebook series is not officially supported by Dynatrace or New Relic. Always verify information against the official [Dynatrace documentation](#) and [New Relic documentation](#).*
